



PROJECT PROPOSAL

A PROPOSED DESIGN OF A TWO STOREY HOUSE

Table of Contents

01	Company Profile Overview of firm background and core expertise
02	Portfolio of Relevant Projects Presentation of Selected Works and Competencies
03	Project Approach and Methodology Strategy and process for project execution
04	Project Timeline Phased schedule of project milestones


05	Professional Fee Proposal Breakdown of service costs and fee
06	Terms of Engagement General Terms and Conditions
07	Accredited Allied Professionals Agreement terms and working conditions
08	References Ways to Contact the Company



ABOUT US

Obra Majoralia is a dynamic, future-oriented architecture studio founded on the conviction that design deeply influences the way we live and experience the world. Grounded in a thoughtful understanding of context—its culture, heritage, and the unique stories of its people—they approach each project with intuition, care, and clarity. Balancing aesthetics and function, their work seeks to create spaces that are meaningful, evocative, and attuned to their surroundings. Every design is a conversation between people and place — thoughtfully shaped to inspire connection, purpose, and longevity.

02 | Portfolio of Relevant Projects



DESIGN PORTFOLIO

This collection showcases a curated selection of residential projects that reflect a thoughtful approach to space, form, and function. Each design emphasizes the unique character of its site and responds to the lifestyle needs of its users. From modern urban dwellings to serene suburban retreats, these works highlight a commitment to spatial clarity, material harmony, and a strong connection between indoor and outdoor living.



03

| Project Approach
and Methodology

I. Design Process and Timeline

		Activities	Deliverables	Estimated Timeline
Schematic Design (SD) (6-8 Weeks)	01	- Client Consultation and Mood Board / Peg Development – Space programming - Feedback loop - Initial Floor Plan Options and Exterior Concept Options - Feedback Loop - Refinement and Finalization of Exterior Design - Final Sign-off for Schematic Design	- Concept Boards (Mood, Material, Inspiration) - Wait for Client Feedback and Queries - Two (2) Floor Plans with Exterior Massing/Design Options - Wait for Client Feedback & Queries - Final Floor Plans and Exterior Design - Wait for Client Feedback & Queries	1 week 3 Days -1 week 2-3 weeks 3 Days -1 week 1-2 weeks 3 Days -1 week
Design Development (DD) (8-13 Weeks)	02	- Development of Interior Design and Selection of Interior Finishes - Feedback Loop - Revisions of interior design and finalization of interior finishes - Feedback loop - Refinement and finalization of exterior design, interior design and material finishes - Final Sign-off for SD	- Initial interior design proposals with preliminary material finishes - Wait for client feedback and queries - Initial interior design proposals with preliminary material finishes - Wait for client feedback and queries - Final floor plans, exterior design, interior design and material swatch board - Wait for client feedback and queries	4-5 weeks 3 Days -1 week 2-3 weeks 3 Days -1 week 1-2 weeks 3 Days -1 week
Contract Documents (CD) (6-9 Weeks)	03	- Detailed architectural drawings for submission and construction - Coordination with engineering trades – Specification writing - OBO-compliant drawings - Final Sign-off for CD	- Complete construction drawings (Architectural, Structural, MEP) - BOQ and technical specifications - OBO set and signed/sealed drawings - Wait for client feedback and queries	6-8 weeks 3 Days -1 week
Bidding Phase (5-8 Weeks)	04	- Assistance in preparing bid documents - Answering contractor inquiries - Optional walkthrough with bidders - Evaluation of contractor proposals (if needed) - Final Sign-off for CD	- Bid package - Clarifications/Addenda - Recommendation on contractor selection (if requested) - Wait for client feedback and queries	1-2 weeks 3-4 weeks 1-2 weeks 3 Days -1 week
Construction Phase	05	- Coordination meetings as needed 4 site visits (1. Start of structural works, 2. Start of architectural works, 3. Finishing phase) - Email/Message-based design clarifications	- Site visit reports - Email logs of queries/clarifications - Punchlist assistance (optional, beyond 3 visits may be billed separately)	Project duration dependent

03 | Project Approach and Methodology

I. Design Process and Timeline Schematic Design (SD)


Step 01 *Client Meeting*

Initial discussion to understand the client's needs, preferences, and vision for the home.



Step 03 *Production of Plans*

Create initial floor plan options with corresponding façade designs to explore possible spatial and aesthetic approaches.

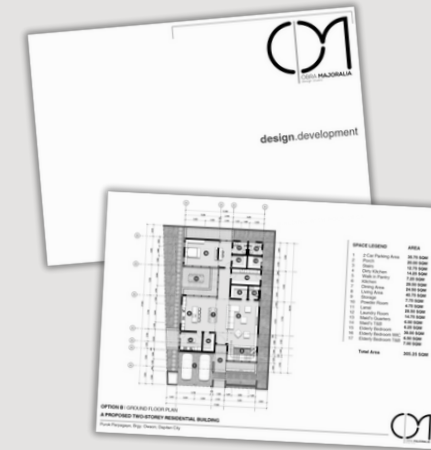

Step 05 *Client Presentation and SD Sign-off to proceed with Design Development*

Present the final schematic design for approval, allowing the team to move forward to the Design Development phase.


Step 02 *Submission of Mood Board/Pegs*

Present mood boards and material references for the house exterior and each space. This aligns the design direction early on, ensuring a smoother and more cohesive design process.



Step 04 *Finalization of Floor Plan and Facade*

Refine and finalize the chosen floor plan and façade design based on client input.

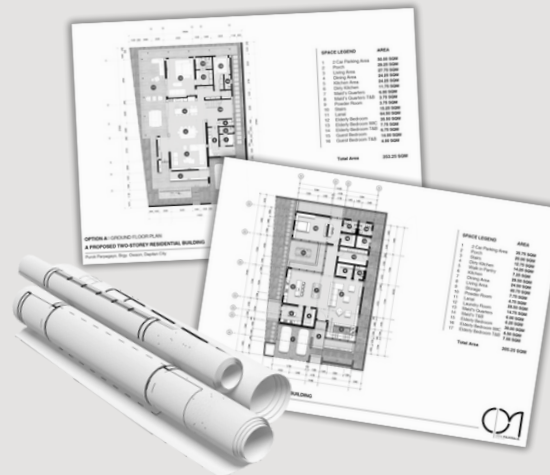

03 | Project Approach and Methodology

I. Design Process and Timeline Design Development Phase (DD)

Step 01

Production of Design Proposal

Production of Final Plans and Exterior Design with Initial Interior Design Proposal.



Step 03

Production of Revised Design Proposal

Refine the design based on client feedback. Updated plans, layouts, and visuals are prepared to reflect the requested changes and improvements.



Step 05

Finalization of Design Proposal

Finalization of Floor Plans and Design Proposal with Production of Material Swatch Board



Step 02

Client Presentation

For design presentation and clarifications on the design and get comments from client.



Step 04

Client Presentation

For design presentation and finalization of design and plans.




Step 06

Client Presentation

Client Presentation and DD Sign-off to proceed with Contract Documents Phase.

03 | Project Approach and Methodology

I. Design Process and Timeline Construction Documents (CD)

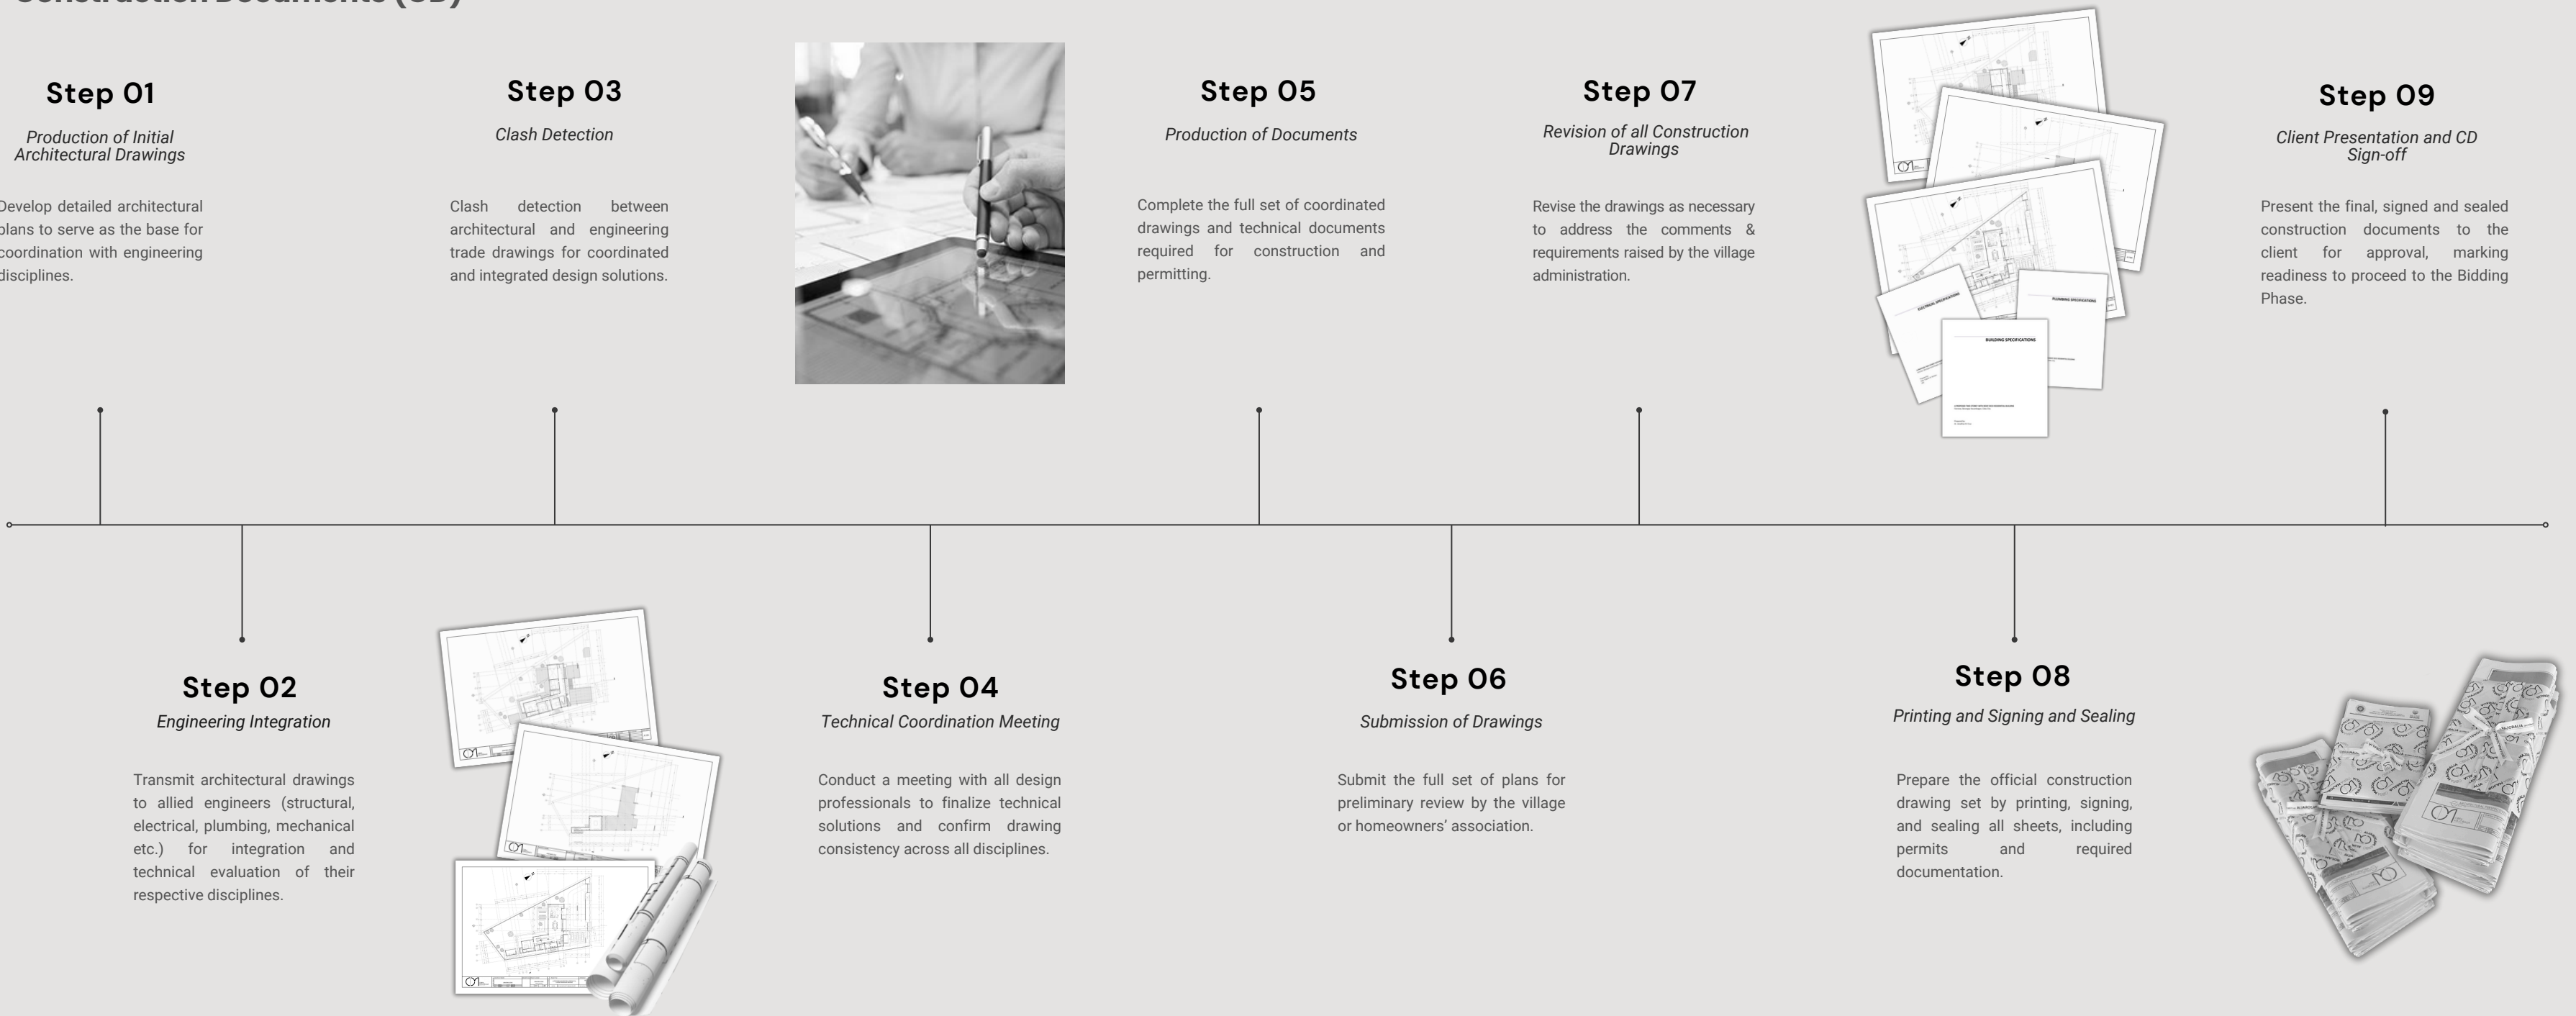

03 | Project Approach and Methodology

I. Design Process and Timeline Bidding Phase

Step 01

Preparation of Bidding Documents

Compiling project details and requirements for bidding.



Step 03

Releasing of Bid Documents to Bidders

Providing official documents to qualified bidders for participation.



Step 05

Entertainment of Bidders' Queries


Addressing bidders' questions during bid preparation period.



Step 07

Evaluation Meeting with Client

Reviewing all bid proposals to decide the contract awardee.

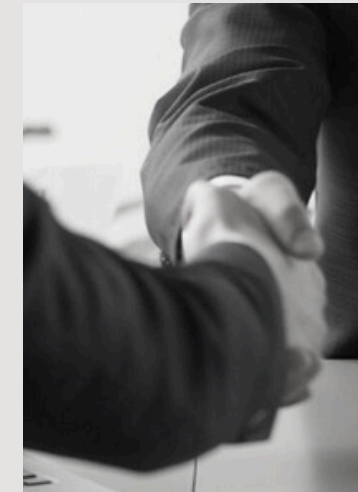

Step 09

Final Meeting with Client and Selected Contractor

Final discussion on groundbreaking, requirements, and contract signing.

Step 02

Alignment Meeting with Client

A meeting to ensure agreement on project goals and expectations.



Step 04

Pre-Bidding Conference

A meeting to clarify bid requirements before submission.



Step 06

Bidders Submission of Bid Proposal


Bidders formally submit their offers for evaluation.



Step 08


Announcement of Winning Bidders

Notifies the selected bidder and informs others of the result via email.

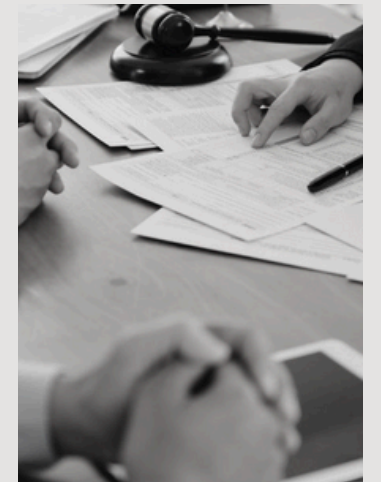


03 | Project Approach and Methodology

I. Design Process and Timeline Construction Phase

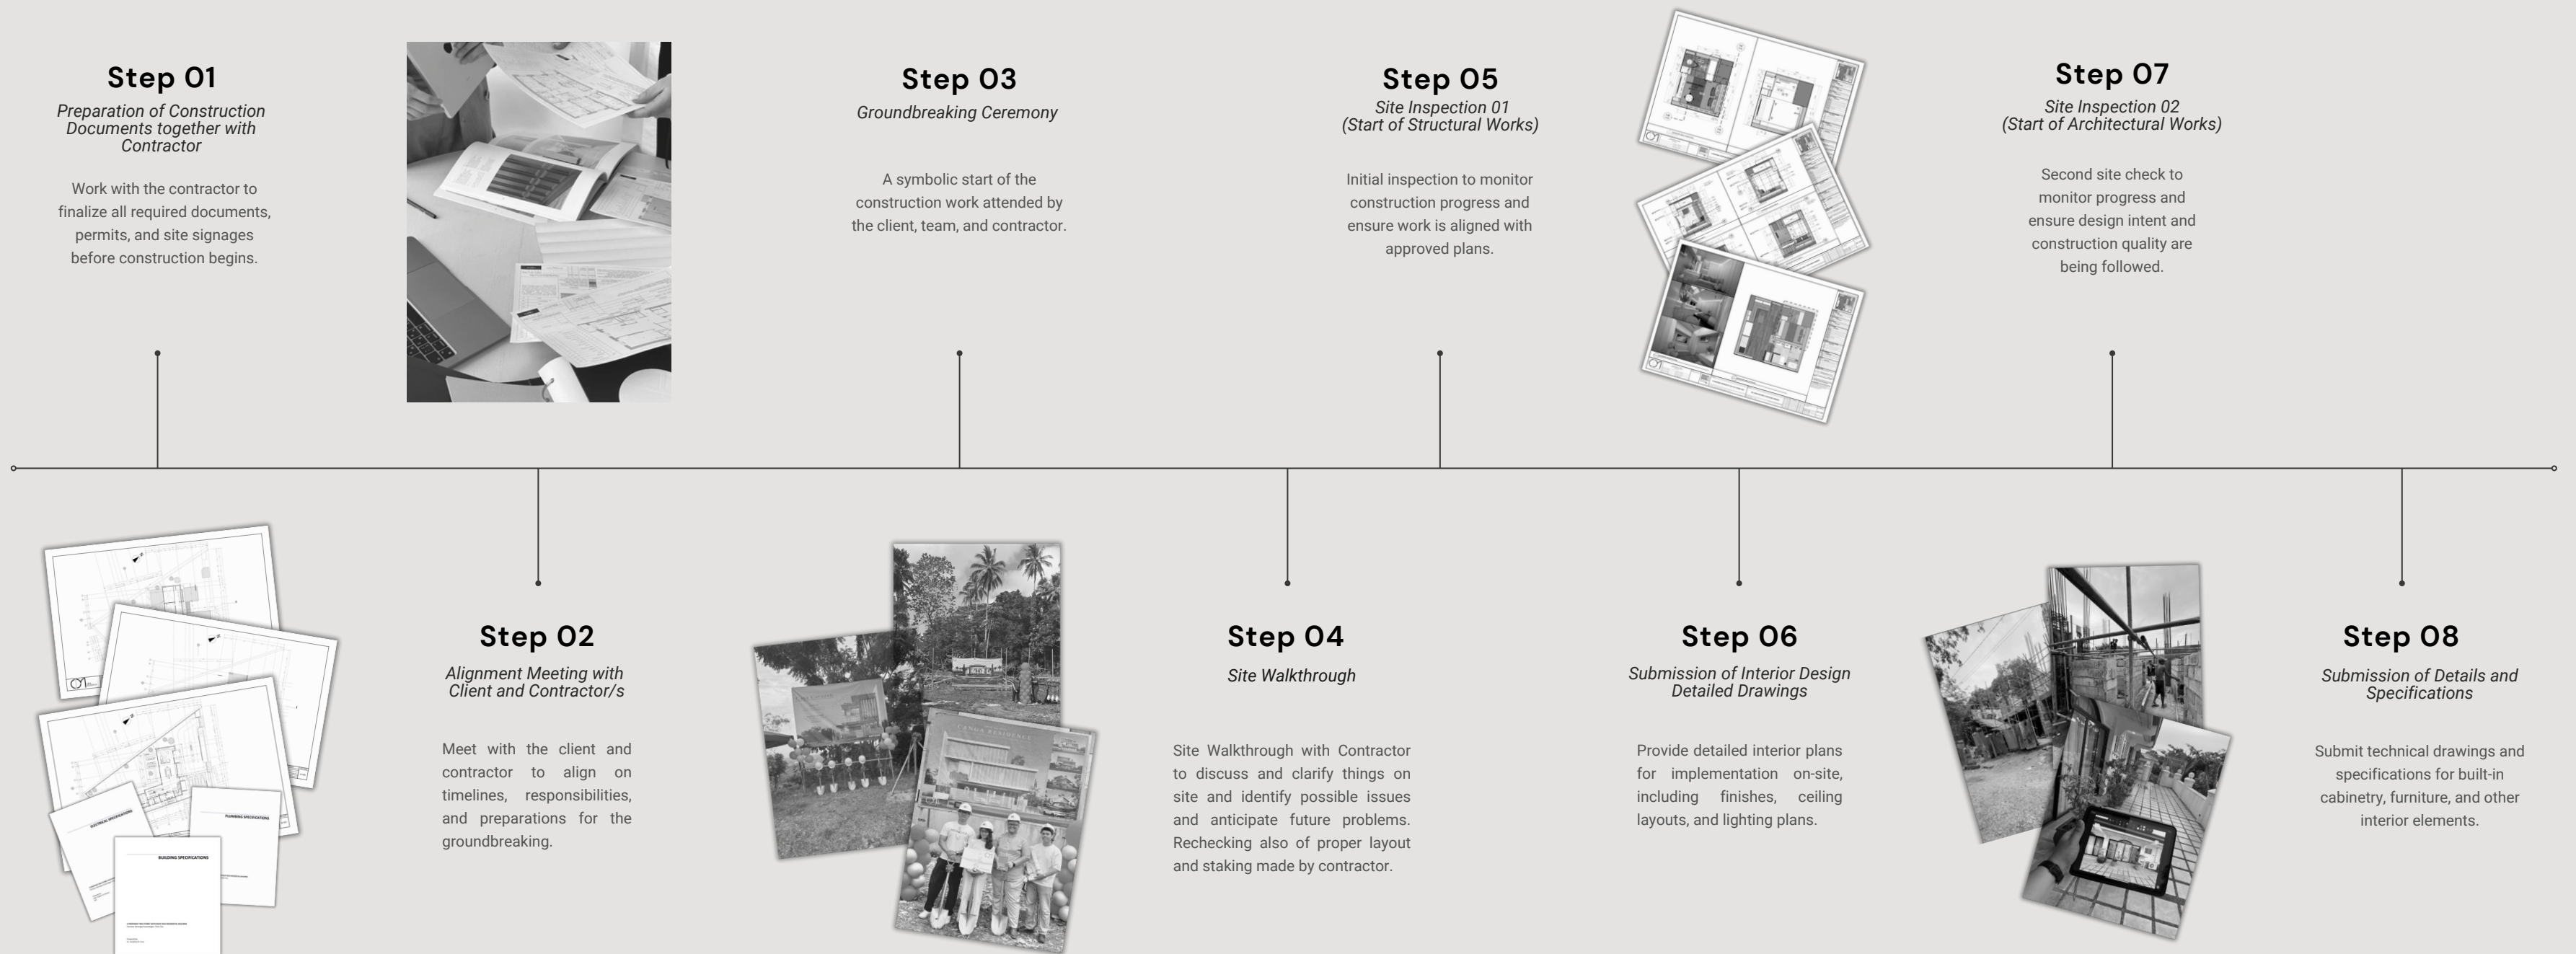

03 | Project Approach and Methodology

I. Design Process and Timeline Construction Phase



03 | Project Approach and Methodology

I. Design Process and Timeline Post-Construction Phase

Step 01

Client Meeting on start of Defects Liability Period (DLP)

Meet with the client to officially begin the Defects Liability Period (usually 3–6 months). Orient them on how to use and maintain features of the home (e.g., switches, systems, materials).



Step 03

Release of Retention

Once all fixes are confirmed, the final payment (retention) is released to the contractor upon approval by the architect and project manager.



Step 05

Submission of Photo book to Client

Deliver a curated photo book to the client, showcasing the home's best angles and design features as a keepsake.



Step 02

Final Inspection After DLP

Conduct a joint inspection with the client and contractor after the DLP to verify that all identified issues have been resolved.



Step 04

Professional Photoshoot of House with staging to be done by us.

Stage and shoot the completed home professionally to document the final design and craftsmanship.

II. Stakeholder Coordination Strategy

Stakeholder	Mode of Engagement	Tools	Frequency
Client	- Regular updates and milestone approvals - Design presentations - Final sign-offs per phase	- Zoom/Google Meet - PDF presentations - Chat/email summaries	Weekly (SD & DD); Bi-weekly or as needed (CD & Construction)
Consultants (Structural, MEP, etc.)	- Regular coordination for inputs - Drawing integration and conflict checks	- Email threads - Shared folder (Google Drive) - CAD/BIM files	Bi-weekly or as needed
Contractor (during bidding/construction)	- Clarifications, site visits, conflict resolution - Material and design conformity checks	- Site meetings - Clarification memos- Viber/WhatsApp/Telegram groups (recommended)	At milestones and upon request
Authorities (OBO, Village Administration, etc.)	Submission of drawings- Responding to regulatory comments	- Hard copy/OBO-compliant sets - Coordination via client or direct (case-dependent)	Once per submission or as needed

III. Site Analysis Methods

METHOD		DESCRIPTION	TOOLS/OUTPUTS
01	Desktop Research	Review of Google Maps, zoning regulations, local development plans	Preliminary site context- Zoning overlays
02	Site Visit and Visual Survey	Observation of sun path, wind direction, terrain, vegetation, views, noise sources, access points	Site documentation photos- Sun and wind diagrams- Opportunities & constraints map
03	Client Consultation	Gather historical info, pain points, aspirations, neighboring lot conditions, flooding history	Client briefing summary
04	Measurements and Mapping	Verify dimensions, existing structures, topography (if applicable)	- As-built sketches, site measurements - Overlay on lot plan
05	Climate and Environmental Data	- Reference local weather and climate data - Assess seasonal rain/flood patterns	- Passive design strategies checklist - Rainwater/flood mitigation input

04 | Project Timeline

Schematic Design (SD)
(6-8 Weeks)

01

Design Development (DD)
(8-13 Weeks)

02

Contract Documents (CD)
(6-9 Weeks)

03

Date	Submission/Activity
August 02, 2025 (Saturday) August 09, 2025 (Saturday) August 13, 2025 (Wednesday) August 29, 2025 (Friday) September 05, 2025 (Wednesday) September 12, 2025 (Wednesday) September 13, 2025 (Saturday)	- Project Kick-off Meeting - Mood Board / Pegs Proposal - Receipt of Client Feedback - Initial Floor Plans w/ Exterior options - Receipt of Client Feedback - Refined and Final Exterior Design - Final Sign-off for SD and Client Meeting
October 08, 2025 (Wednesday) October 15, 2025 (Wednesday) October 29, 2025 (Wednesday) November 03, 2025 (Wednesday) November 10, 2025 (Monday) November 14, 2025 (Friday)	- Submission of Initial Interior Design Proposal - Receipt of Client Feedback - Revised Interior Design Proposal - Receipt of Client Feedback - Refined and Final Exterior Design and Interior Design and final Material Swatch Board - Final Sign-off for DD and Client Meeting
December 12, 2025 (Friday) December 13, 2025 (Saturday) January 05, 2026 (Monday) January 09, 2026 (Friday) January 14, 2026 (Wednesday)	- Submission of Initial Construction Drawings to Village Administration for Preliminary Approval - End-of-Year Client Meeting - Receipt of Village Admin Comments and Feedback - Printing of Revised Construction Drawings based on Village Administration comments. - Release of Signed and Sealed Final Construction Drawings

04 | Project Timeline

		Date	Submission/Activity
Bidding Phase (5-8 Weeks)	04	January 15, 2026 (Thursday)	• Releasing of Bid Documents to Bidders and Client Meeting
		January 21, 2026 (Wednesday)	• Pre-Bid Conference
		February 11, 2026 (Wednesday)	• Submission Deadline for Bidders' Proposals
		February 18, 2026 (Monday)	• Final Result of Bidding and Awarding
		February 20, 2026 (Monday)	• Final Sign-off for Bidding Phase w/ Contractor
Construction Phase	05	Feb 22, 2026 (Sunday) *Bing Wu day—marked auspicious date in Feng Shui specifically for "Break Ground for Building" and "Laying the Foundation Stone."	• Ground Breaking Ceremony
		February 27, 2026 (Friday)	
		March 11, 2026 (Wednesday)	• Submission of Construction Drawings and other Contract Documents to Office of the Building Office (OBO) for Building Permit Application (by Contractor)
		March 27, 2026 (Friday)	• Site Inspection 01 - Start of Structural Works
		June 10, 2026 (Wednesday)	• Release of Building Permit from OBO
		July 22, 2026 (Wednesday)	• Submission of Interior Design Detailed Construction Drawings w/ adjustments based on actual site measurements
		September 18, 2026 (Friday)	• Site Inspection 02 - Start of Architectural Works
		October 19-23, 2026 (Friday)	• Submission of Joinery/Cabinetry Detailed Drawings and Furniture Details/Specifications for supplier/s quotation
		December 11, 2026 (Friday)	• Materials Sourcing/Meeting with Suppliers
		December 14, 2026 (Friday)	• Site Inspection 03 - Middle of Architectural Works
		January 06, 2027 (Wednesday)	• Year-end Alignment Meeting with Contractor/s, Client and Suppliers.
		January 27, 2027 (Wednesday)	• Start-of-Year Client Meeting
		February 24, 2027 (Wednesday)	• Finalization Meeting with Suppliers and Subcontractors for Architectural/Interior Works
		March 19, 2027 (Friday)	• Site Inspection 04 - Finishing of Architectural Works
		March 29-31, 2027 (Mon-Wed)	• Punchlisting of work by Contractor/s and Suppliers
		April 02, 2027 (Friday)	• Final Site Walkthrough on rectified punchlist.
		April 04, 2027 (Sunday) * Auspicious for moving and residence relocation based on Feng Shui	• Staging of Furniture, Decors and Other Items (for Photoshoot and Turnover)
			• Meeting with Client and Contractor/s for finalization of all deliverables needed before Turnover.
			• Home Turnover and Blessing

04 | Project Timeline

Post- Construction Phase	06	Date	Submission/Activity
		• July 03, 2027 (Saturday)	• Client meeting at the start of the Defects Liability Period (typically 3–6 months depending on the contract) to orient the client on the technical aspects of the house—such as switches, systems, and proper maintenance procedures.
		• July 31, 2027 (Saturday)	• Final House Inspection and Meeting with Client and Contractor after DLP (Put stock photo of a house tour/inspection)
		• August 07, 2027 (Saturday)	• Professional Photoshoot of the house, with staging to be handled by our team.
		• September 04, 2027 (Saturday)	• Submission of Photo Book to Client

05

| Professional Fee Proposal

1.0 Scope of Work

The scope of work shall cover the architectural/interior design of the aforementioned project including the following structures/spaces:

	AREA COVERED	FLOOR AREA
1.0	Ground Floor	150 sqm
2.0	Second Floor	150 sqm
3.0	Roof Deck	150 sqm
Total Area		± 450 sqm
Excluded: Should you need other services not specifically stated above; it will be quoted separately and will be covered by separate contract.		

05 | Professional Fee Proposal

1. Acceptance/Design Phase

1.1.1 Schematic Design

1. Project Background
2. Site Inspection
3. Design Pegs
4. Coordination with the Building Administration, if applicable, and Owner/Client to know the requirements of the project and design brief.
5. Design Conceptualization and Space Planning which would aid in coming up with the design solutions for the Project that are subject to approval by the Owner/Client.
6. Submit to the Owner Preliminary Drawings and/or Sketches showing the general concept of the project which includes but not limited to the following:

- **Concept Boards/Mood Boards**
- **Floor Plan/s with Furniture, Fixture and Equipment Layout**
- **Rendered Exterior Perspectives/3D Model**

1.1.2 Design Development

1. Development Process of the approved Conceptual Design Studies.
 - **Revised Floor Plan/s with Furniture, Fixture and Equipment Layout**
 - **Lighting and Power Provisions**
 - **Rendered Perspective of Exterior and Interior Spaces**
 - **Limited to three (3) Minor Revisions only.**
2. Recommends to the Owner, if necessary, the services of Specialized Allied Professionals and coordinates with such as to the requirements of the project.
3. Coordinates with other Allied Engineering teams engineering systems needed for the project such as but not limited to:
 - **Mechanical**
 - **Electrical**
 - **Electronics and Communication**
 - **Sanitary/Plumbing**
 - **Structural**
4. Coordinates with various suppliers, contractors and subcontractors for the selection of the types of materials and finishes to be used in the project.

05 | Professional Fee Proposal

2. Contract Documentation Phase

1. Submits up to **Eight (8) Printed Copies and PDF File** of Construction Drawings and technical specifications. The construction drawings are as follows:

Detailed Architectural and Interior Design Drawings:

- Architectural Floor Plans
- Complete Blow-up Plans of all Included Areas
- Elevations and Sections indicating Heights, Clearances & Material Specification
- Materials Specifications
- All other details necessary for construction

Signed and Sealed Allied Trades' Drawings:

- Electrical
- Plumbing/Sanitary
- Electronics and Communications
- Mechanical
- Structural

2. Prepares and collates all the documents from all parties involved that are required for the building permit application.

3. Construction Phase

1. **Makes decisions in the interpretation** of the Contract Documents and assists in the resolution of any questions which may arise.
2. Submits up to **two (2) printed Copies and PDF File** of Interior Design Drawings and technical specifications. The construction drawings are as follows:
 - **Interior Design Detailed Construction Drawings**
 - **Joinery/Cabinetry Detailed Drawings**
 - **Furniture Details and Specifications**
 - **Materials List and Suppliers Directory**
3. Periodic site visits based on construction milestones of up to **four (4) visits**, start of structural works, start or architectural works, middle of architectural works and finishing of architectural works. The Architect's regular services **do not include weekly, exhaustive or continuous 8-hour on-site observation** and **cannot be responsible for the Constructor's failure to carry out the work in accordance with the Contract Documents**. For site visit of projects located beyond 100 km from the studio's office, the transportation and accommodation shall be shouldered by the client. Moreover, an additional fee shall be charged if full-time supervision is desired by the Client and would either be considered as a different contract.

05 | Professional Fee Proposal

4. Construction Phase

4. **Makes reports to the Client** based on observations made on such site visits of any defects and deficiencies noted in the work of the sub-contractors.
5. If required, **the Architect shall assist the Client** in the assessment of the work and progress of the contractor and shall determine the amount due the contractor based on such assessment upon the contractor's application for payments.
6. **Checks and approves** samples, schedules, shop drawings and other requirements submitted by the subcontractors subject to and in accordance with the descriptive information and provisions of the Contract Documents.

05 | Professional Fee Proposal

2.0 Professional Fee Computation

The Architect’s Fee is based on the projected Gross Floor Area (450 sqm) and the scope items stipulated in the General Scope of Architectural Services. Should the actual gross floor area increase beyond the initial projection, additional charges shall apply proportionately. Likewise, where the Architect is required to render additional services outside the agreed scope, corresponding compensation shall be required.

This competitive rate is extended as a special consideration for this bidding process, and reflects our studio’s genuine interest in collaborating with the Client on a creatively, sustainably, and contextually meaningful home.

Option 01: Architectural + Interior Design + Engineering Trades

AREA COVERED	FLOOR AREA	REGULAR PROFESSIONAL FEE (PHP 3,200/SQM)
Two - Story Residence	450 sqm	Php 1,440,000.00
Initial Computed Professional Fee		Php 1,440,000.00
Discounted Professional Fee		Php 1,350,000.00

Option 02: Architectural + Interior Design

AREA COVERED	FLOOR AREA	FLOOR AREA (PHP 2,500/SQM)
Two - Story Residence With Roof Deck	450 sqm	Php 1,125,000.00
Initial Computed Professional Fee		Php 1,125,000.00
Discounted Professional Fee		Php 1,025,000.00

06 | Terms of Engagement

Option 01: Architectural + Interior Design + Engineering Trades

1.0 Breakdown of Fees and Schedule of Payments

PHASE	TASKS / DELIVERABLES	PROFESSIONAL FEE
Acceptance / Schematic Design Phase	• Project Definition • Concept Boards/Mood Boards • Furniture, Fixtures and Equipment Layouts • Rendered Exterior Perspectives	20% of Professional Fee = Php 270,000.00
Design Development Phase	• Revised Floor Plan/s with Furniture, Fixture and Equipment Layout • Lighting and Power Provisions • Rendered Perspective of Exterior and Interior Spaces • Sample Material Swatches • Materials Sourcing • Coordination with Suppliers and Contractors. • Engineering Trades Provisions	20% of Professional Fee = Php 270,000.00
Contract Documents Phase	• Eight (8) Sets Signed and Sealed Construction Drawings: ◦ Architectural ◦ Electrical ◦ Plumbing/Sanitary ◦ Electronics and Communications ◦ Mechanical ◦ Structural • Prepare Documents for Village Building Permit Application. • Building Permit Processing.	30% of Professional Fee = Php 405,000.00

06 | Terms of Engagement

PHASE	TASKS / DELIVERABLES	PROFESSIONAL FEE
Bidding Phase	• Preparing of Bid Documents • Evaluation of Bid Proposals • Assist Client in choosing the contractor	5% of Professional Fee = Php 67,500.00
Design Development Phase	• Revised Floor Plan/s with Furniture, Fixture and Equipment Layout • Lighting and Power Provisions • Rendered Perspective of Exterior and Interior Spaces • Sample Material Swatches • Materials Sourcing • Coordination with Suppliers and Contractors. • Engineering Trades Provisions	20% of Professional Fee = Php 270,000.00
Construction Phase	• Four (4) Periodic Site Visits during construction — start of structural works, start or architectural works, middle of architectural works and finishing of architectural works • Makes reports on defects and deficiencies on site. • Assist the Client in the assessment of the work and progress of the contractor. • Checks and approves samples, schedules, shop drawings. • Submission of Two (2) Sets of Printed Interior Design Drawings. • Submission of Joinery/Cabinetry Drawings and Furniture Specifications. • Materials Sourcing and Meeting with Suppliers • Submission of Shop Drawings as per Contractor/s request.	20% of Professional Fee = Php 270,000.00 (Progress Billing Divided to 4 billed per site inspection)
Project Turnover	• Punchlisting • Staging / Setting up of Furniture, Furnishings, & Accessory. • Photoshoot for Portfolio • Turn over of the Project	5% of Professional Fee = Php 67,500.00
Total Contract Price		Php 1,350,000.00

06 | Terms of Engagement

Option 02: Architectural + Interior Design

PHASE	TASKS / DELIVERABLES	PROFESSIONAL FEE
Acceptance / Schematic Design Phase	• Project Definition • Concept Boards/Mood Boards • Furniture, Fixtures and Equipment Layouts • Rendered Exterior Perspectives	20% of Professional Fee = Php 205,000.00
Design Development Phase	• Revised Floor Plan/s with Furniture, Fixture and Equipment Layout • Lighting and Power Provisions • Rendered Perspective of Exterior and Interior Spaces • Sample Material Swatches • Materials Sourcing • Coordination with Suppliers and Contractors. • Engineering Trades Provisions	20% of Professional Fee = Php 205,000.00
Contract Documents Phase	• Eight (8) Sets Signed and Sealed Architectural Drawings • Prepare Documents for Village Building Permit Application. • Building Permit Processing.	30% of Professional Fee = Php 307,500.00

06 | Terms of Engagement

PHASE	TASKS / DELIVERABLES	PROFESSIONAL FEE
Bidding Phase	• Preparing of Bid Documents • Evaluation of Bid Proposals • Assist Client in choosing the contractor	5% of Professional Fee = Php 51,250.00
Construction Phase	• Four (4) Periodic Site Visits during construction — start of structural works, start or architectural works, middle of architectural works and finishing of architectural works • Makes reports on defects and deficiencies on site. • Assist the Client in the assessment of the work and progress of the contractor. • Checks and approves samples, schedules, shop drawings. • Submission of Two (2) Sets of Printed Interior Design Drawings. • Submission of Joinery/Cabinetry Drawings and Furniture Specifications. • Materials Sourcing and Meeting with Suppliers • Submission of Shop Drawings as per Contractor/s request.	20% of Professional Fee = Php 205,000.00 (Progress Billing Divided to 4 billed per site inspection)
Project Turnover	• Punchlisting • Staging / Setting up of Furniture, Furnishings, & Accessory. • Photoshoot for Portfolio • Turn over of the Project	5% of Professional Fee = Php 51,250.00
Total Contract Price		Php 1,025,000.00

*This section presents the various phases of design which is accompanied by a defined set of deliverables to ensure clarity and alignment of expectations throughout the design process. Corresponding payments shall be made prior to the commencement of each phase to facilitate the timely and continuous progress of the work.

06 | Terms of Engagement

2.0 General Terms and Conditions

2.1 Change Order and Variation

No amendment to this Agreement shall be valid unless made in writing and signed by both the Architect/Interior Designer and the Client. Verbal or informal modifications shall not be binding. This ensures that all changes are mutually agreed upon and legally enforceable.

2.2 Exclusions

Site Visit/s upon project construction/implementation that exceed the stipulated number of periodic visits shall be charged accordingly. Per diem rate for additional site visits is at Php 4,000 and does not constitute an extensive 8-hour site supervision. Should you require more consistent and comprehensive site monitoring, a separate Site Supervision Contract can be arranged. This will be based on a fixed monthly rate and will already account for travel expenses, allowances, and contingencies—ensuring efficient and reliable oversight throughout the construction period.

2.3 Termination and Cancellation of Contract

In the event that the services of the Architect/Interior Designer are suspended or terminated—whether in whole or in part—by the Client or due to causes beyond the Architect's control, the Architect/Interior Designer shall be entitled to full compensation for all professional services rendered and reimbursable expenses incurred up to the date and phase of suspension or termination. Such compensation shall be due and payable immediately.

Furthermore, the Architect/Interior Designer reserves the right to suspend or terminate this Agreement at any time should the Client engage in unprofessional conduct, including but not limited to verbal abuse, unreasonable demands, consistent non-compliance with agreed processes, or any behavior that compromises the Architect's professional integrity or well-being. In such cases, the same compensation terms shall apply.

06 | Terms of Engagement

2.0 General Terms and Conditions

2.4 Ownership of Documents

Drawings and specifications and other contract documents duly signed, stamped or sealed, as instruments of service, are the intellectual property and documents of the Architect/Interior Designer, whether the object for which they are made is executed or not. It shall be unlawful for any person to duplicate or to make copies of said documents for use in the repetition of and for other projects or buildings, whether executed partly or in whole, without the written consent of the Architect/Interior Designer or author of said documents.

2.5 Terms of Payment

The payment terms for this contract stipulate that payments will be billed before the commencement of each project phase. A detailed invoice outlining the costs for the upcoming phase will be issued for payment. The client is required to make the payment in full before work on the respective phase begins. Failure to make timely payments may result in project delays.

3.0 Client Responsibilities

- Provide the designers with a Wish List and Design Brief (e.g. Concept parameters, Project references, guidelines and other relevant information necessary for the project)
- Extra copies requested by the Client in addition to the number of deliverables stated above shall be to the Client's account.
- Scope of work not indicated in this agreement will be treated as an additive and is subject to a separate agreement to the Client's account (e.g. Project Management, etc.)
- The owner shall pay for any pertinent fees, permits, and licenses related to the Project.

07 | Accredited Allied Professionals

01

STRUCTURAL ENGINEER

Engr. Arzen Ann Christine R. Caguitla

Senior Structural Designer, WTA Architecture and Design Studio

- Over 8 years of professional experience, specializing in retail and residential developments
- Currently leading a structural project in Damar Village
- Serves as our trusted structural engineer for Metro Manila and Luzon-based projects
- Known for her precision, reliability, and collaborative approach in delivering structurally sound and design-integrated solutions

02

PLUMBING, MECHANICAL AND FIRE PROTECTION

Leonides M. Paragsa Design and Consultancy Services

- With 13 years of professional experience, the firm has delivered a wide range of projects—from private residences to high-rise office towers
- Recognized as one of the most respected design consultancies in Cebu
- Recipient of the Outstanding Cebuano Award (TOCA) 2019 for Design Consultancy
- A valued collaborator in over 30 successful projects, including residential, retail, and office developments

03

ELECTRICAL ENGINEER



Engr. Eugene Declaro

In-house Registered Electrical Engineer (REE)

- Trusted in-house REE with strong technical expertise in residential and commercial electrical systems
- Has collaborated with us on approximately 11 projects, ensuring safe, efficient, and code-compliant electrical design and implementation

08 | References

Client Testimonials



Contact Us

Get in touch with us for more inquires and questions.

general inquires

✉ obra.majoralia@gmail.com

☎ +63 967 234 0041

social media platforms

fb.com/obra.majoralia

@obra.majoralia

address

📍 Unit 917b, Meridian by Avenir, Golam Drive,
Brgy. Kasambagan, Cebu City 6000

Obra **Majoralia**



Casa Rossi
Damar Village, Quezon City



Thank You!



obra.majoralia@gmail.com



+63 967 234 0041



Unit 917b, Meridian by Avenir, Golam Drive, Brgy. Kasambagan, Cebu City 6000

